

WEEKLY CONSTRUCTION REPORT

Project: SJEC HVAC Upgrade
1623 Carmel Rd,
Charlotte NC, 28226

Week Ending: 8/10/24

Distribution List:

St. John's Episcopal Church: David Dwyer, Jeff Cummins, John Horn

SC Hondros & Associates: Alex Scheffer, Dan Riter, Sam Kleto, Tom Griffin, Mark Murray

This Week:

- Continued to remove ACT ceiling to expose the work area for ductwork and electrical conduit.
- Electricians pulling wire and installing the panel boxes in the mechanical room.
- Organ has been protected by a specialty organ contractor.

Next Week:


- Continue ductwork and chiller pipe demolition.
- Continue removing FCUs on second floor.
- Begin installing new ductwork.

Inspections:

- Structural steel will require special inspections and a pre-con meeting with the city. SJEC has released the special inspector.

Schedule and Milestone Updates:


- The chiller has been permanently shut down due to leaks in the existing pipe. This allows us to drain down all chiller pipes and accelerate the planned schedule.

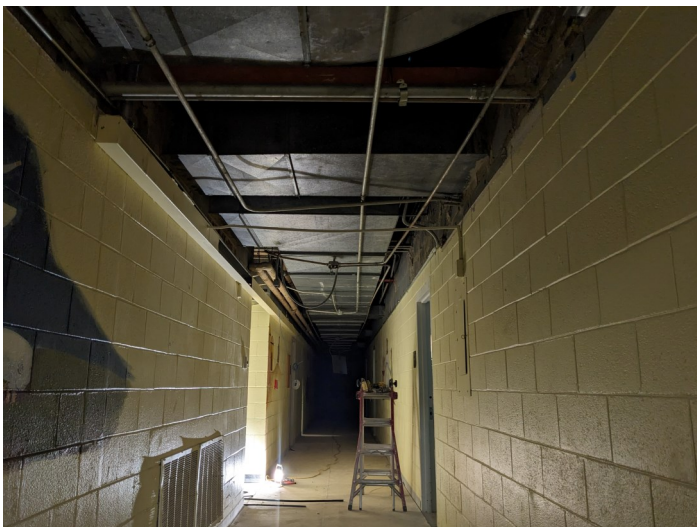

Corridor grid and tile removed



Electrical panel boxes have been installed.



WEEKLY CONSTRUCTION REPORT

Project: SJEC HVAC Upgrade
1623 Carmel Rd,
Charlotte NC, 28226

Week Ending: 8/10/24

Distribution List:

St. John's Episcopal Church: David Dwyer, Jeff Cummins, John Horn

SC Hondros & Associates: Alex Scheffer, Dan Riter, Sam Kleto, Tom Griffin, Mark Murray



Corridor grid and tile removed



FCU and chiller piping removed.



Existing ductwork removed in classroom.



FCUs removed on the 1st floor.
