

WEEKLY CONSTRUCTION REPORT

Project: SJEC HVAC Upgrade
1623 Carmel Rd,
Charlotte NC, 28226

Week Ending: 9/7/24

Distribution List:

St. John's Episcopal Church: David Dwyer, Jeff Cummins, John Horn, Peter Floyd

SC Hondros & Associates: Alex Scheffer, Dan Riter, Sam Kleto, Tom Griffin, Mark Murray

This Week:

- Completed demo in mechanical room 1 & 3
- Installed panel interiors in mechanical room 2
- Started ductwork in room 136

Inspections:


- Waiting on the special inspector to verify that the pre-inspection is complete so that we can call in for inspections.

Next Week:

- Continue installing ductwork.
- Continue installing wiring on the 2nd and 1st floor.
- Begin ceiling demo on the 2nd floor.

Schedule and Milestone Updates:

- New VRF units should start arriving in the next week or 2.
- Pew refinisher will begin work 9/16/24.

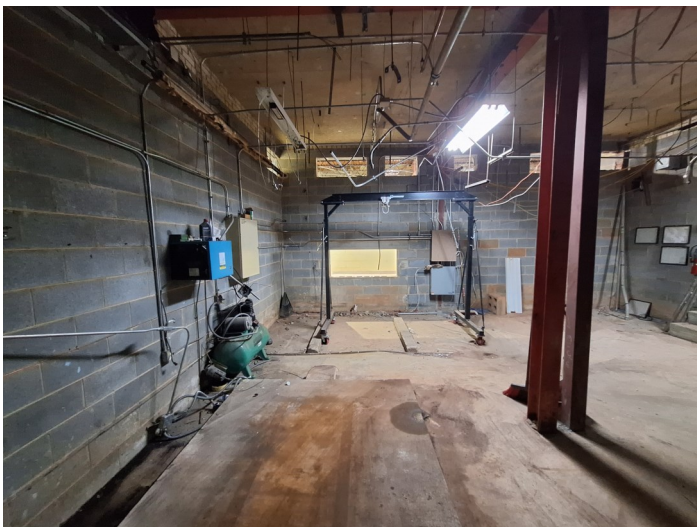

Boiler room demo complete



Tie in new ductwork to the existing.
