

WEEKLY CONSTRUCTION REPORT

Project: SJEC HVAC Upgrade

1623 Carmel Rd,
Charlotte NC, 28226

Week Ending: 8/31/24

Distribution List:

St. John's Episcopal Church: David Dwyer, Jeff Cummins, John Horn, Peter Floyd

SC Hondros & Associates: Alex Scheffer, Dan Riter, Sam Kleto, Tom Griffin, Mark Murray

This Week:

- Existing boiler and mechanical room equipment has been removed.
- Staging new ductwork.
- Installing electrical conduit, pulled main feeder wire.

Inspections:

- Special Inspection Pre-construction meeting has been completed.

Next Week:

- Continue ductwork and chiller pipe demolition.
- Continue with electrical installation.
- Begin installing new ductwork.

Schedule and Milestone Updates:


- Pews will be removed the 3rd week of September.
- 2nd floor demolition will begin in the next 2-3 weeks. Need rooms cleared for construction.



Main entrance access



Existing roof conditions



WEEKLY CONSTRUCTION REPORT

Project: SJEC HVAC Upgrade
1623 Carmel Rd,
Charlotte NC, 28226

Week Ending: 8/31/24

Distribution List:

St. John's Episcopal Church: David Dwyer, Jeff Cummins, John Horn


SC Hondros & Associates: Alex Scheffer, Dan Riter, Sam Kleto, Tom Griffin, Mark Murray



Installing new electrical conduit



Equipment removed in boiler room

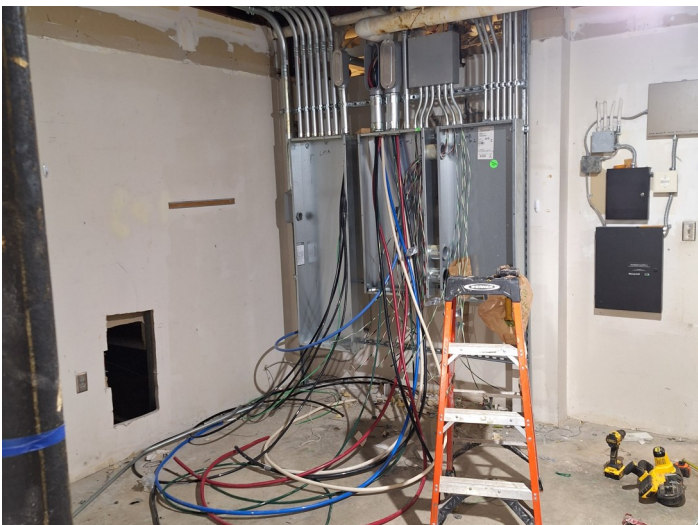

Pulling main feeder wire



Ductwork removed in hallway
