

WEEKLY CONSTRUCTION REPORT

Project: SJEC HVAC Upgrade

1623 Carmel Rd,
Charlotte NC, 28226

Week Ending: 9/13/24

Distribution List:

St. John's Episcopal Church: David Dwyer, Jeff Cummins, John Horn, Peter Floyd

SC Hondros & Associates: Alex Scheffer, Dan Riter, Sam Kleto, Tom Griffin, Mark Murray

This Week:

- Ceiling tile removed on the 2nd floor.
- FCU's removed on the 2nd floor.
- Electrical panel interiors installed and circuits landed.

Inspections:


- Plumbing inspector is good with covering the condensate drains if they are within 2' of a main drain line. Otherwise they will need to install a cleanout.

Next Week:

- Storage containers deliver 9/16 for McPhail
- Norman from PcPhail will be on-site 9/17 at 2pm to review the pew placement with the church.
- Continue mechanical and electrical work on both floors.

Schedule and Milestone Updates:


- Power shutdown scheduled for 9/27 at 8am.
- Domestic water in Mechanical Room 2 will need to be rerouted away from the power panels.
- Chimney demo tentatively scheduled for 9/23

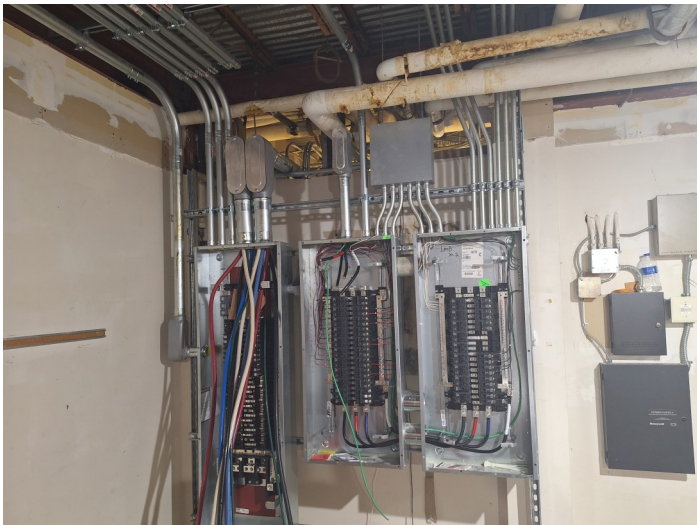

Panel interiors installed



Ceiling removed in the choir room



WEEKLY CONSTRUCTION REPORT

Project: SJEC HVAC Upgrade
1623 Carmel Rd,
Charlotte NC, 28226

Week Ending: 8/31/24

Distribution List:

St. John's Episcopal Church: David Dwyer, Jeff Cummins, John Horn

SC Hondros & Associates: Alex Scheffer, Dan Riter, Sam Kleto, Tom Griffin, Mark Murray



Ceiling removed in the choir corridor



FCU removal in the breezeway



Ductwork installation



Ceiling removed in the breezeway
